


POSSIBLE
LIBRARY
ADDITION

24
MONTHS

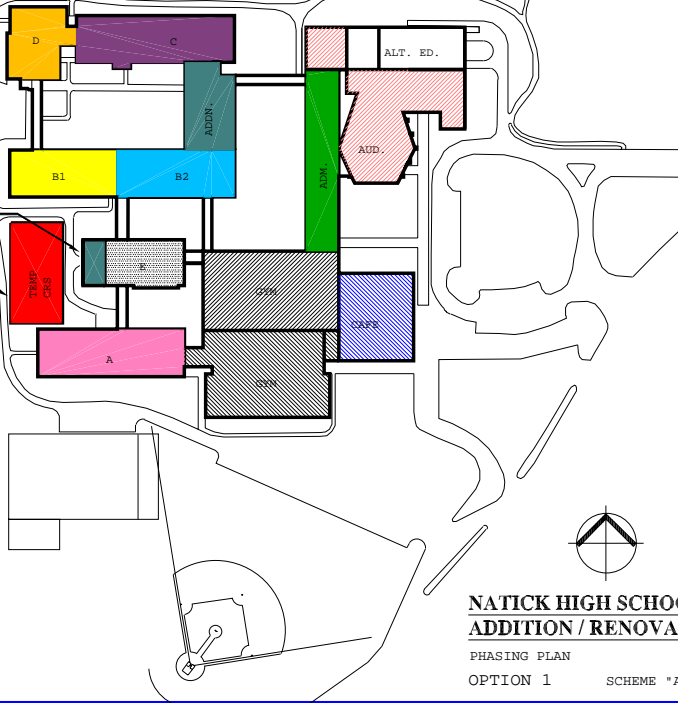

NATICK HIGH SCHOOL
ADDITION / RENOVATION


PHASING PLAN

OPTION 1

SCHEME "A"

AREA / MONTHS	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20		
Temporary Classrooms					In place 24 months																	
Addition																						
Part A Lower																						
Part A Upper																						
Part B 1 Upper & Lower																						
Part B 2 Upper & Lower																						
Part C Lower																						
Part C Upper																						
Part D Upper & Lower																						
Part E Upper & Lower	Schedule with School Administration																					
Shops	Schedule with School Administration																					
Administration																						
Administration																						
Administration																						
Gymnasium Part 1	First Summer																					
Gymnasium Part 2	Second Summer																					
Cafeteria	First Summer																					
Auditorium	Second Summer																					

POSSIBLE
LIBRARY
ADDITION
12
MONTHS

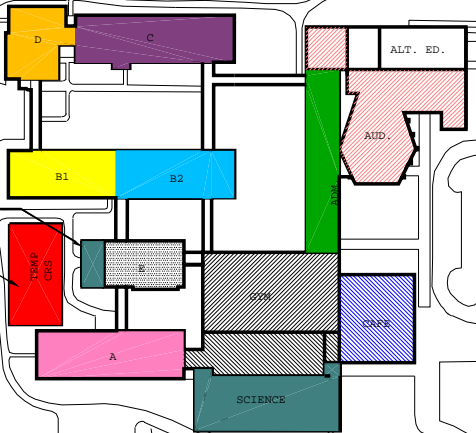

**NATICK HIGH SCHOOL
ADDITION / RENOVATION**

PHASING PLAN

OPTION 1

SCHEME "B"

AREA / MONTHS	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20
Temporary Classrooms																				
Library Addition & Science																				
Part A Upper & Lower																				
Part B 1 Upper & Lower																				
Part B 2 Upper & Lower																				
Part C Lower																				
Part C Upper																				
Part D Upper & Lower																				
Part E Upper & Lower																				
Administration																				
Administration																				
Administration																				
Gymnasium Part 1																				
Gymnasium Part 2																				
Cafeteria																				
Auditorium / Music																				
